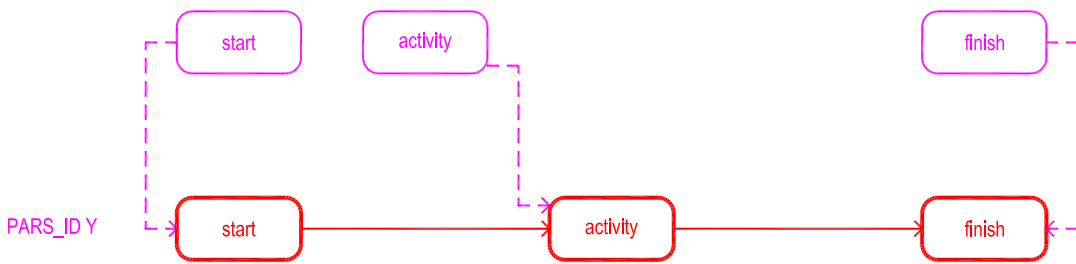# project schedule from the program schedule (proposed)

1. create program schedule (sample consists of 2 projects: PARS_IDs X & Y)

PARS_ID X

| start | → | activity | | milestone | → | finish |

PARS_ID Y

| start | | activity | | finish |

2. F9 program schedule (program driving path determined - red) (F9 w/o "ignore relationships")
3. isolate PARS_ID Y (modify only external predecessor tasks to constrained SVTs)

PARS_ID Y

| start | activity | | finish |

PARS_ID Y

| start | → | activity | → | finish |

4. F9 PARS_ID Y schedule (project driving path determined - red) (F9 w/ "ignore relationships")
5. create PARS_ID Y JSON

sample program schedule

program-05	DOE
program-04	program_office	program_office
program-03	site	site
program-02	federal	PARS_program	GPP	ops	regulatory
program-01 PARS	PARS_project	PARS_project
program-00 P6	P6_project	P6_project	P6_project	P6_project	P6_project	P6_project	P6_project	logic ties

P6_01   P6_02   P6_03   P6_04   P6_05   P6_06   P6_07
